


# Construction Last 2 Weeks – Treatment Building foundation on Tyco property





# Construction Last 2 Weeks – Pipes Connecting Wells & Junction Vaults 1 & 2 on Tyco property

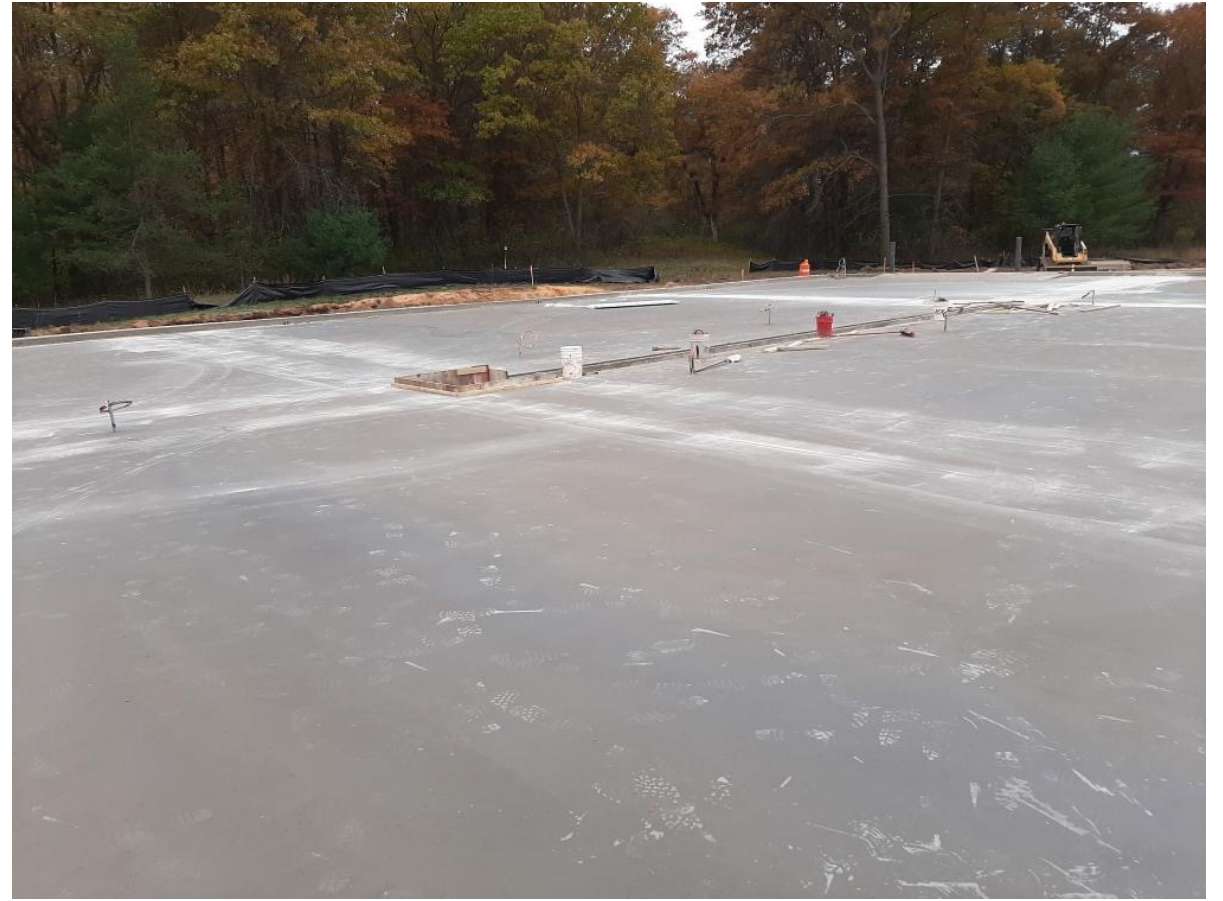



# Construction Last 2 Weeks - Wells 3, 4 & 5 on Access Road

## Extractions Wells Installed

- EX-3, -4 & 5 (white) on new access road along Ditch B & piezometers/monitoring wells (yellow) to monitor performance



# Planned Construction - Next 2 weeks+

## 1. Treatment Building Construction

- Walls being erected

## 2. Horizontal Drilling to Install Conveyance Piping

- In Road Right-of-Ways including Oak View Rd., & Edwin St., to connect wells 6, 7 & 8
- Expect a horizontal drill rig & other equipment in each area for 1-3 days
- Impacts to traffic – road closed except to local traffic
- Work is anticipated to take approximately 2 weeks to complete

