Fire Technology Center (FTC) PFAS Remediation Office Hours December 15, 2021




GETS Route – Well Locations & Piping Routes

= 9 extraction wells

= Conveyance pipes (to be installed)

= Conveyance pipes (installed)

= Ditch B

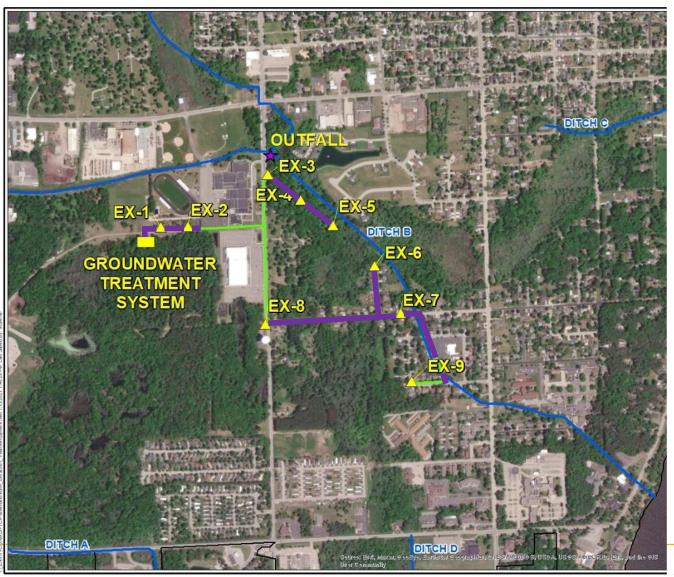



GETS Construction Last 2 Weeks – Treatment Building



Work continued on finishing exterior and starting interior of Treatment Building on FTC property





GETS Construction Last 2 Weeks – Installation of Conveyance Pipes & Junction Vaults

- Horizontal drilling on <u>Edwin</u> now complete
- Installing junction vaults at <u>Edwin & Oak View</u>
- Pulled small groundwater conveyance piping thru large conductor casing on <u>Edwin & Oak View</u>
- Horizontal drilling on <u>James</u>







Planned Construction - Next 2 weeks+

- Continue interior work in <u>Treatment Building</u> on Tyco property
- Horizontal drilling on <u>Florence</u> to install conductor casing for groundwater conveyance piping from EX-9
- Finishing vault installation on <u>Edwin & Oak View</u>
 - Impacts: Ongoing installation of various mechanical and electrical components (roads will <u>not</u> be blocked)
- Vaults & conveyance piping installations on <u>James and</u> <u>Florence</u>.
 - <u>Impacts:</u> Horizontal drill rig & other equipment in each area; roads closed except to local traffic








Safety First During Construction

- Community Outreach and Notifications
- Traffic Control

Site Security





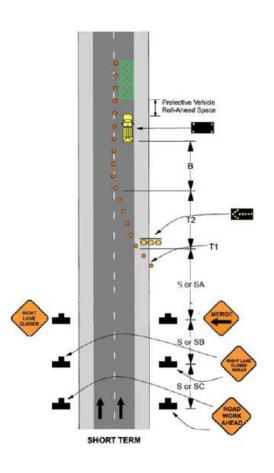



Key Project Elements & Timing

Project Phases Estimated Start – End Date

Permitting	Ongoing throughout Construction Phase
Off-Site Construction	Late summer thru March 2022
Major Construction in Rights-of-Way Installation of conveyance piping, extraction wells and control boxes	October thru early January 2022
Drill Extraction Wells	Complete (except for EX-7 – estimated Dec 2021)
Minor construction around extraction wells	January thru March 2022
On-Site Construction	Late summer thru March 2022
Access Road Construction For access to 3 extraction wells & outfall location	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	October – December 2021
Delivery & Installation of Filtration Technology	December 2021 through March 2022
Complete Construction & Startup GETS	Goal: Late Spring 2022



Questions & Feedback



If you have any other questions, you can always call our dedicated phone line at (715) 582-7100 or send an email via our website, www.tycomarinette.com/ Contact Us

