Fire Technology Center (FTC) PFAS Remediation Office Hours January 12, 2022



# **GETS Route – Well Locations & Piping Routes**

#### = 9 extraction wells

- = Conveyance pipes (to be installed)
- = Conveyance pipes (installed)
- = Interior pipes (installed)

Outfall

GROUNDWATER TREATMENT SYSTEM



#### **GETS Construction Last 4 Weeks – Treatment Building**



#### Work continued on interior of Treatment Building on FTC property






### GETS Construction Before Holiday - Finished Installation of Conveyance Pipes on Residential Streets

- Finished Horizontal Drilling and installation of Conveyance
  Piping on Florence St
- Set Vault on <u>James St.</u>
- Installed Vaults & Conveyance Piping on <u>Edwin St</u>.
  <u>& Oak View St.</u>
- Installed well EX-7 on Edwin St



## **GETS Construction Next 2 Weeks**


- Start Horizontal Directional Drilling below ground along <u>Pierce Ave</u>. near Marinette High School
  - Associated utility locating ("potholing") Wed. Jan. 12;
  - Scheduled to take about 3 weeks
- Follow-up work on well EX-6 at end of Oak View St.
- Continue interior work on <u>Treatment Building</u> on FTC property connecting electric, heat; installing sprinklers
- Impact of work along Pierce Rd.
  - Temporarily closed south entrance/exit to High School Tuesday, Jan. 11
  - Drilling rig on High School land west of Pierce St.
  - Truck traffic in area
  - No lane closures on Pierce St.

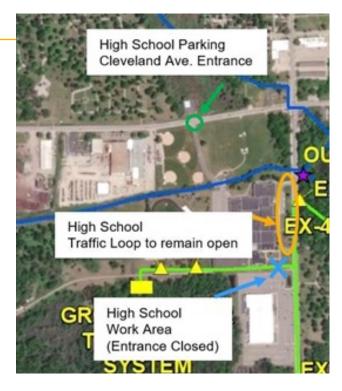

# **Safety First During Construction**

- Community Outreach and Notifications
- Traffic Control
- Site Security



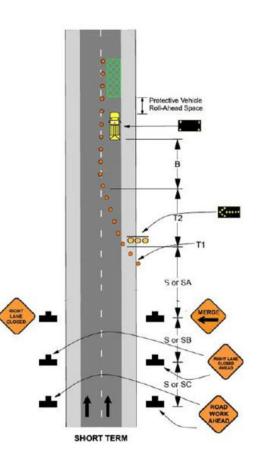



# **Key Project Elements & Timing**

Project Phases	Estimated Start – End Date
Permitting	Ongoing throughout Construction Phase
Construction	Late summer 2021 thru January 2022
Construction in Rights-of-Way	
Installation of conveyance piping, extraction wells and control boxes	October thru January 2022
Access Road Construction	
For access to 3 extraction wells & outfall location	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	October – January 2022
Delivery & Installation of Filtration Technology	January through March 2022
Complete Construction & Begin Startup of GETS	Goal: 1 <sup>st</sup> half of 2022



### **Questions & Feedback**



If you have any other questions, you can always call our dedicated phone line at (715) 582-7100 or send an email via our website, www.tycomarinette.com/ Contact Us
