
Fire Technology Center (FTC) PFAS Remediation Office Hours February 23, 2022



GETS Route – Well Locations & Piping Routes



- = Conveyance pipes (to be installed)
- = Conveyance pipes (installed)
- = Interior pipes (installed) = Ditch B = Outfall

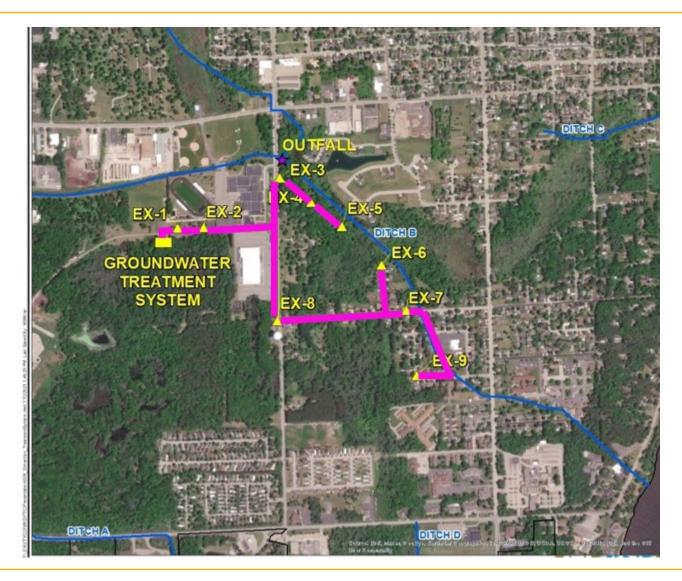

GETS Construction Last 2 Weeks – Treatment Building


Work continued on interior of Treatment Building located on FTC property, including:

- Placement of initial delivery of treatment vessels,
- Groundwater conveyance piping piping
- Installation of permanent electrical service to building
- Motor control center installation

Mechanical work in treatment building will continue through startup anticipated in June



GETS Construction Last 2 Weeks – Treatment Building

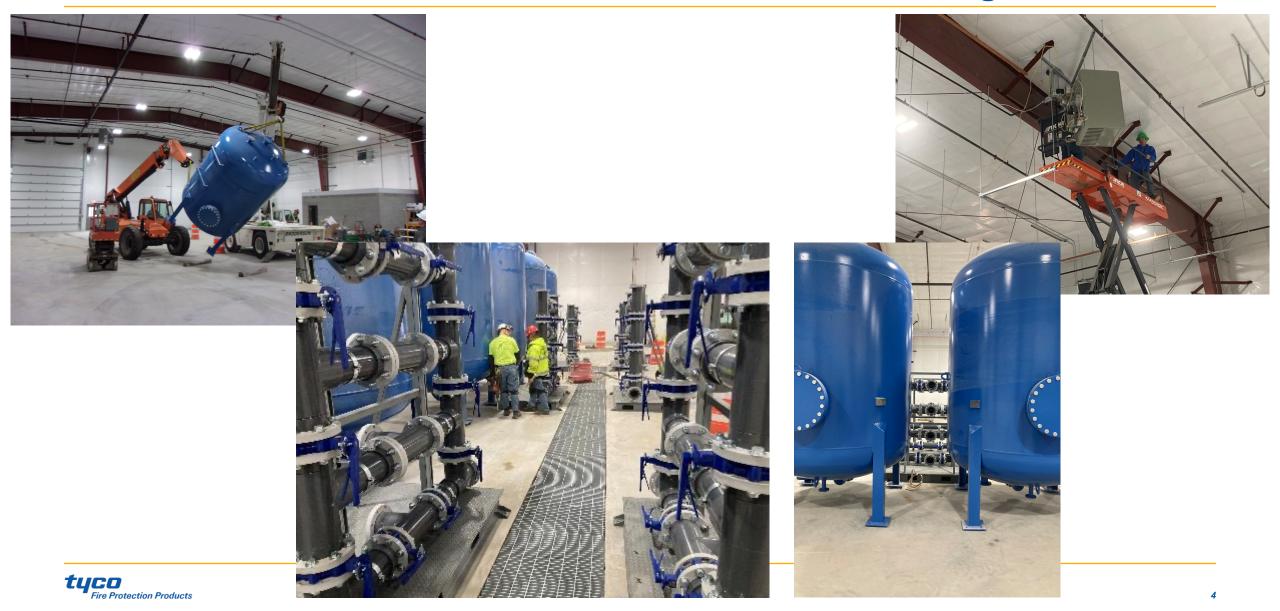

GETS Construction – Offsite piping/construction - Last 2 Weeks

- All directional drilling is complete
- All underground vaults have been installed
- Temporarily repaired high school driveway and reopened driveway on 2/17
- Rip rap placed and Ditch B outfall complete
- After this week no more major offsite construction until final surface restorations to be completed in the Spring
 - Minor electrical controls and interior plumbing will be completed at well vaults through the spring and early summer



GETS Construction – Offsite piping/construction - Last 2 Weeks



GETS Construction Moving Forward


- Most of the remaining GETS work will be in the treatment building
- Minor plumbing (including pump installation) and electrical work (on and off) at extraction wells through spring and early summer
 - EX-6 at the end of Oak View Rd
 - Ex-7 in Edwin St east of Oak View Rd
 - EX-9 at Florence and Richard St
- Temporarily road repairs will be made permanent in the Spring
- Decreased office hours frequency



Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security



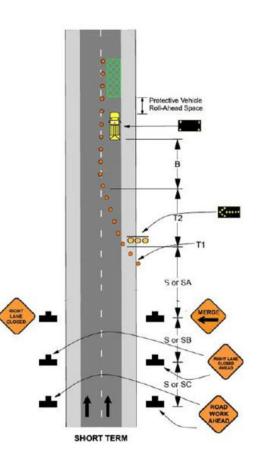



Key Project Elements & Timing

Project Phases	Estimated Start – End Date
Permitting	Ongoing throughout Construction Phase
Construction	Late summer 2021 thru February 2022
Construction in Rights-of-Way	
Installation of conveyance piping, extraction wells and control boxes	October thru February 2022
Access Road Construction	
For access to 3 extraction wells & outfall location	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	October – February 2022
Delivery & Installation of Filtration Technology	January through March 2022
Complete Construction & Begin Startup of GETS	Goal: 1 st half of 2022



Questions & Feedback



If you have any other questions, you can always call our dedicated phone line at (715) 582-7100 or send an email via our website, www.tycomarinette.com/ Contact Us
