
Fire Technology Center (FTC) PFAS Remediation Office Hours Nov. 17, 2021




GETS Route – Well Locations & Piping Routes

▲= 9 extraction wells

= Convenyance pipes



= Outfall

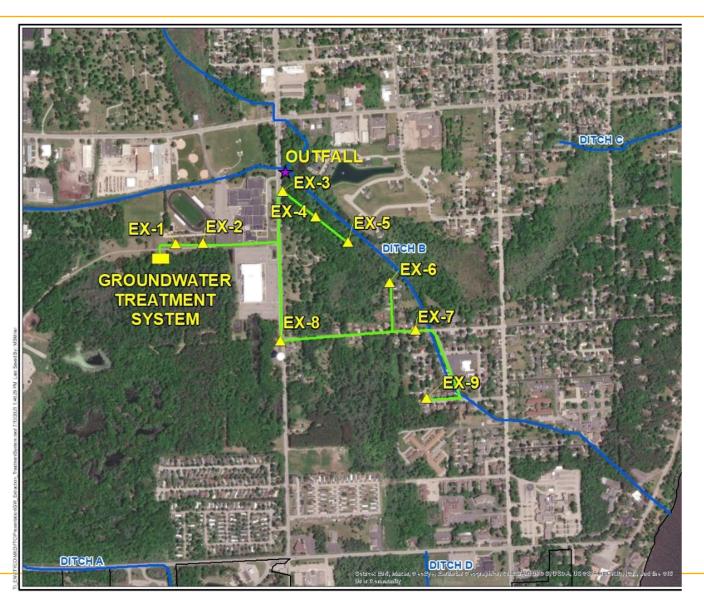

Construction Last 2 Weeks – Treatment Building structure & walls went up.





Construction Last 2 Weeks – Installation of Conveyance Pipes

- Pipes connecting extraction wells EX-3, -4 & -5 on Access Road
- Horizontal Drilling on Oakview Rd

& Edwin St. related to wells EX-6









Planned Construction - Next 2 weeks+

- Finish installation around walls and of Treatment Building roof on Tyco property
- Horizontal Drilling to install the conductor casing for the groundwater conveyance piping
 - Work is ongoing in road rights-of-way on Edwin St. between extraction Wells EX-7 & -8
 - Work may begin in road rights-of-way of Florence & James St. to connect to EX-9
 - Horizontal drill rig & other equipment in each area
 - Impacts to traffic road closed except to local traffic
- May conduct work at the EX-3, -4, -5 & -6 wellheads








Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security



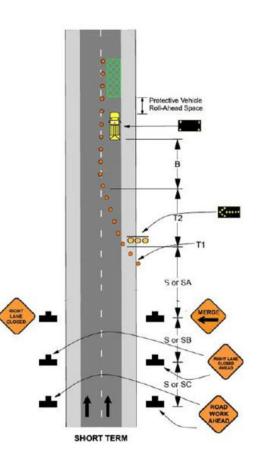



Key Project Elements & Timing

Project Phases	Estimated Start – End Date
Permitting	Ongoing throughout Construction Phase
Construction	Late summer to December 2021
Construction in Rights-of-Way	
Installation of conveyance piping, extraction wells and control boxes	October through early December 2021
Access Road Construction	
For access to 3 extraction wells & outfall location	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	October/November
Delivery & Installation of Filtration Technology	December 2021 through March 2022
Complete Construction & Startup GETS	Goal: March 2022

Questions & Feedback



If you have any other questions, you can always call our dedicated phone line at (715) 582-7100 or send an email via our website, www.tycomarinette.com/ Contact Us
