







**Fire Technology Center (FTC)
PFAS Remediation Office Hours
January 26, 2022**

tyco
Fire Protection Products

GETS Route – Well Locations & Piping Routes

-  = 9 extraction wells
-  = Conveyance pipes (to be installed)
-  = Conveyance pipes (installed)
-  = Interior pipes (installed)
-  = Ditch B
-  = Outfall



GETS Construction Last 4 Weeks – Treatment Building



Work continued on interior of Treatment Building on FTC property



GETS Construction – Last 2 Weeks

- Completed follow-up work on well EX-6 at end of Oak View St.
- Started installing Conveyance Piping along Pierce Rd.
 - Temporarily closed south entrance/exit to High School – started Tuesday, Jan. 11
 - Drilling rig on High School land west of Pierce St.
 - Truck traffic in area
 - No lane closures on Pierce St.




GETS Construction Next 2 Weeks

- Continue Horizontal Drilling on land along and west of Pierce Ave. near Marinette High School
 - Started Wed. Jan. 12 & scheduled to take 4 weeks due to weather
- Continue & complete interior work on Treatment Building on FTC property – then begin installing treatment components
- Impact of work along Pierce Rd.
 - Temporarily closed south entrance/exit to High School until Feb. 11
 - Drilling rig on High School southern access drive land west of Pierce
 - Truck traffic in area
 - Will need to temporarily close about 100 ft of Pierce Ave. along south end of High School/north end of Rec Center for safety so can lay pipe out east across Pierce since too cold to bend it
 - **For about 8 hrs in second week of Feb – stay tuned for specifics**



Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security

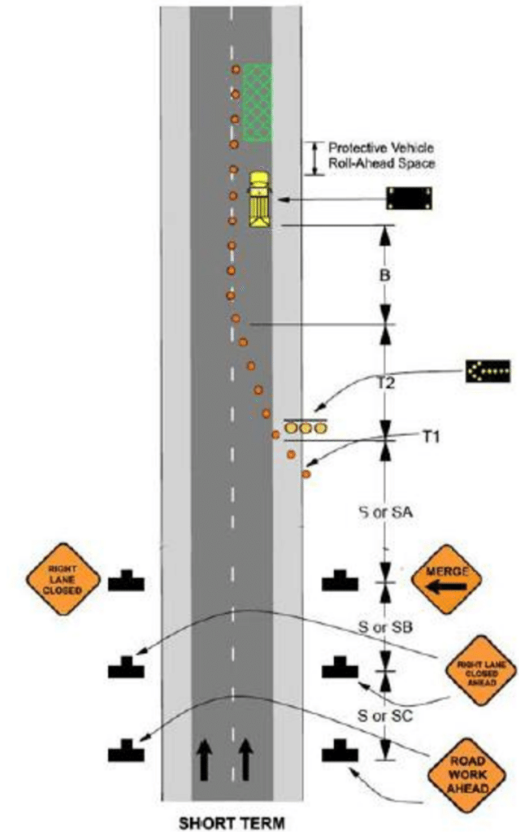

Key Project Elements & Timing

Project Phases	Estimated Start – End Date
Permitting	Ongoing throughout Construction Phase
Construction	Late summer 2021 thru January 2022
Construction in Rights-of-Way Installation of conveyance piping, extraction wells and control boxes	October thru January 2022
Access Road Construction For access to 3 extraction wells & outfall location	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	October – January 2022
Delivery & Installation of Filtration Technology	January through March 2022
Complete Construction & Begin Startup of GETS	Goal: 1 st half of 2022

Questions & Feedback



If you have any other questions, you can always call our dedicated phone line at [\(715\) 582-7100](tel:7155827100) or send an email via our website, [www.tycomarinette.com/Contact Us](http://www.tycomarinette.com/ContactUs)
