








**Fire Technology Center (FTC)  
PFAS Remediation Office Hours  
February 9, 2022**

***tyco***  
*Fire Protection Products*

# GETS Route – Well Locations & Piping Routes

-  = 9 extraction wells
-  = Conveyance pipes (to be installed)
-  = Conveyance pipes (installed)
-  = Interior pipes (installed)
-  = Ditch B
-  = Outfall

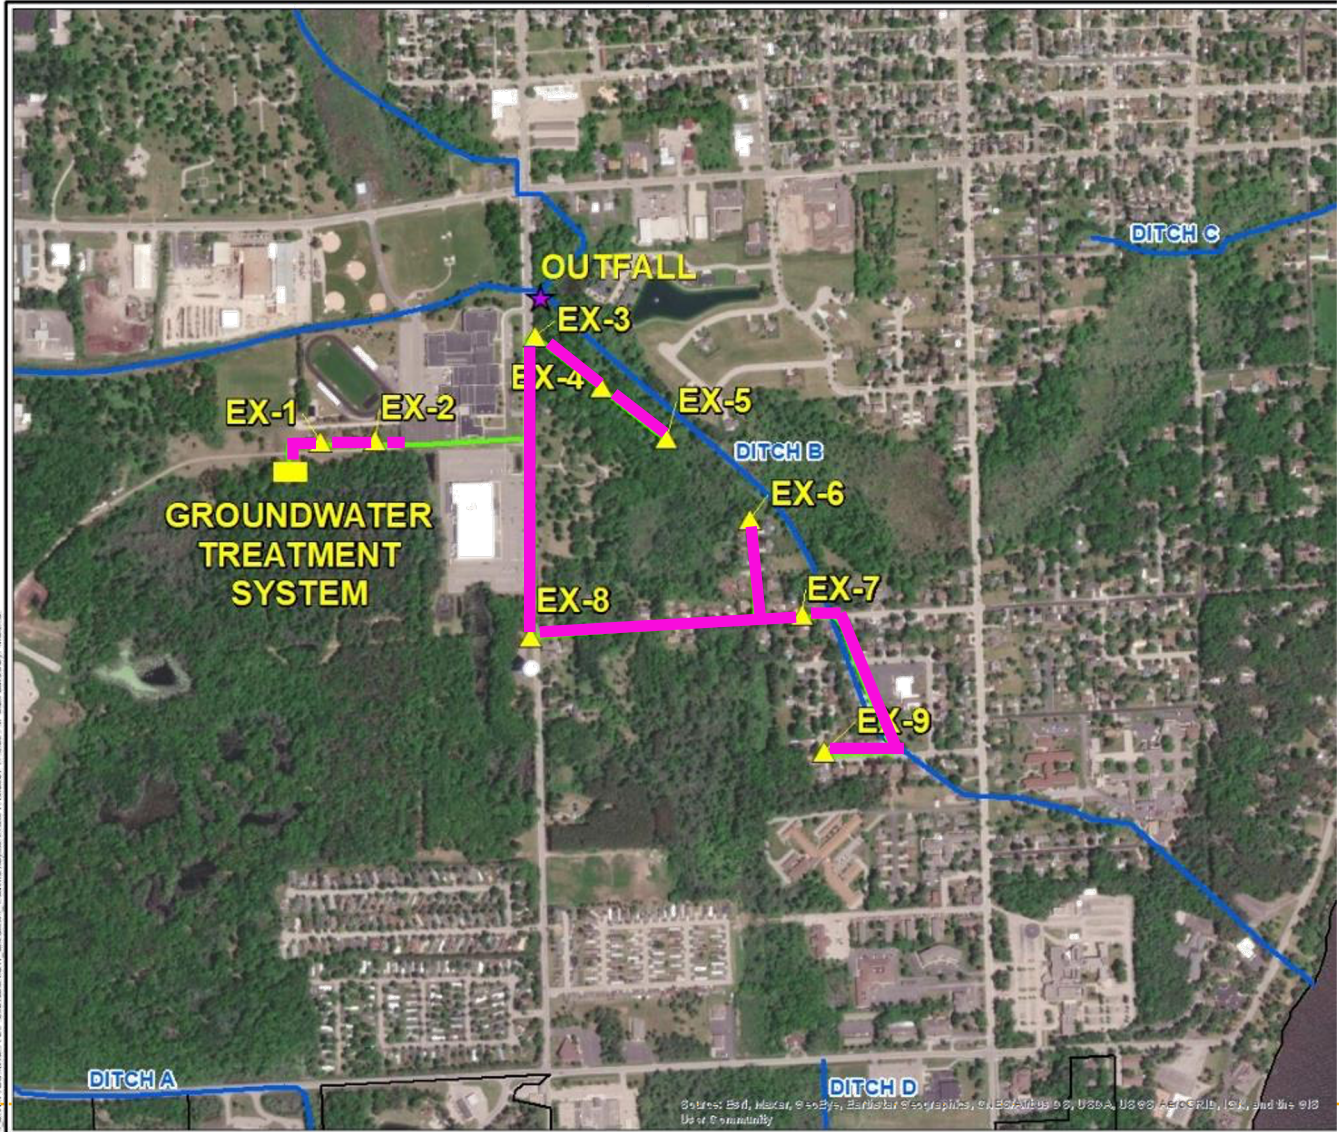

# GETS Construction Last 2 Weeks – Treatment Building

---

Work continued on interior of Treatment Building on FTC property, including pouring pads for heavy filtering tank equipment.

Will continue for next 2 weeks



# GETS Construction – Last 2 Weeks


---

- Started installing Conveyance Piping along Pierce Rd.
  - Temporarily closed south entrance/exit to High School – started Tuesday, Jan. 11
  - Drilling rig on High School land west of Pierce St.
  - Truck traffic in area
  - No lane closures on Pierce St.




# GETS Construction Next 2 Weeks

- Continue Horizontal Drilling on land along and west of Pierce Ave. near Marinette High School
  - Started Wed. Jan. 12 & scheduled to take 4 weeks due to weather
- Impact of work along Pierce Rd.
  - Temporarily closed south entrance/exit to High School until Feb. 25
  - Drilling rig on High School southern access drive land west of Pierce
  - Will need to temporarily close about 100 ft of Pierce Ave. along south end of High School/north end of Rec Center for safety so can lay pipe out east across Pierce since too cold to bend it
    - Today, Wed. Feb. 9 from 7am to evening

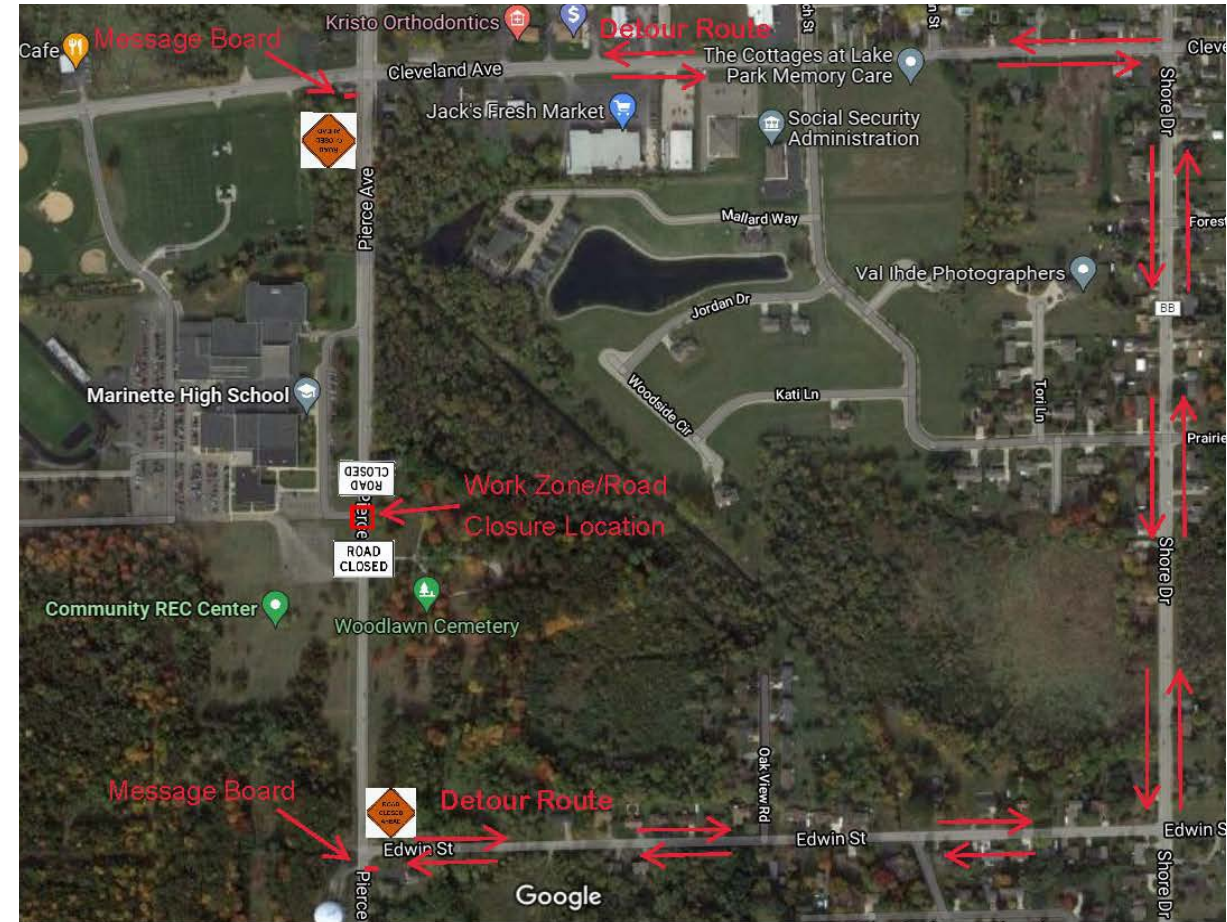

# Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security

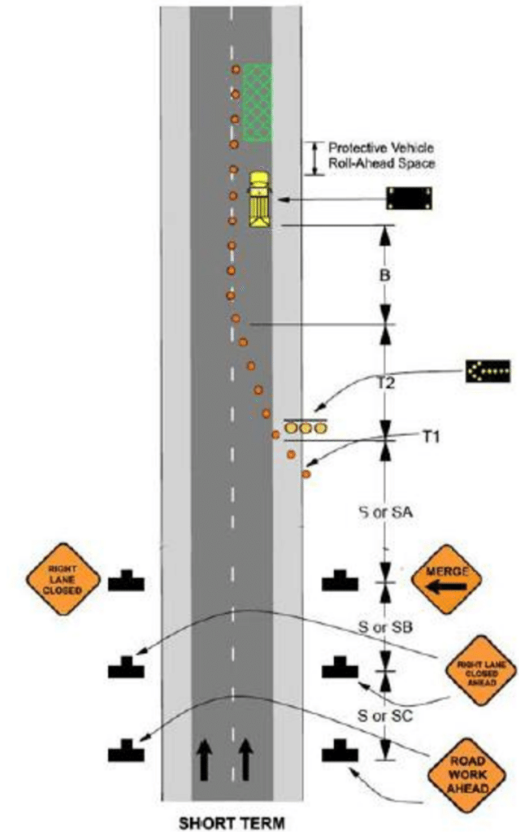

# Key Project Elements & Timing

Project Phases	Estimated Start – End Date
<b>Permitting</b>	Ongoing throughout Construction Phase
<b>Construction</b>	Late summer 2021 thru February 2022
Construction in Rights-of-Way Installation of conveyance piping, extraction wells and control boxes	October thru February 2022
Access Road Construction For access to 3 extraction wells & outfall location	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	October – February 2022
Delivery & Installation of Filtration Technology	January through March 2022
<b>Complete Construction &amp; Begin Startup of GETS</b>	Goal: 1 <sup>st</sup> half of 2022

# Questions & Feedback

---



If you have any other questions, you can always call our dedicated phone line at [\(715\) 582-7100](tel:7155827100) or send an email via our website, [www.tycomarinette.com/Contact Us](http://www.tycomarinette.com/ContactUs)
