





**Fire Technology Center (FTC)
PFAS Remediation Office Hours
May 25, 2022**

tyco
Fire Protection Products

GETS Route – Well Locations & Piping Routes

-  = 9 extraction wells
-  = Conveyance pipes (to be installed)
-  = Ditch B
-  = Outfall



GETS Construction Last Four Weeks

- Work continued in interior of Treatment Building located on FTC property, including:
 - All carbon & resin treatment vessels previously installed
 - Air compressor installed
 - Ongoing installation of electrical lines and mechanical piping
 - Epoxied treatment building floor
- All exterior pipelines have been installed and pressure tested, and vaults moisture sealed
- Electrical and mechanical piping completed within extraction well vaults

GETS Construction Last Four Weeks

- Pulled power cables to extraction well vaults
- Installed control panels at all extraction wells
- Additional rock and gravel added to new access road and associated well vault locations
- Repaired depressions in Oak View Road that formed along the borehole path
- Seeded disturbed excavation areas with grass and straw

GETS Construction – Upcoming activities

- Continued electrical and piping in GETS building
- Poly break tanks, clarifier and green sand filter installed over the next two weeks
- Final restorations of roads scheduled to be done by mid-June
- Installation of extraction well pumps scheduled to be done mid-June
- WPS electric and gas service upgrades on Edwin and Oak View ongoing - *Unrelated to GETS project*

GETS Construction– Treatment Building



GETS Construction– Treatment Building




GETS Construction – Extraction Wells



Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security

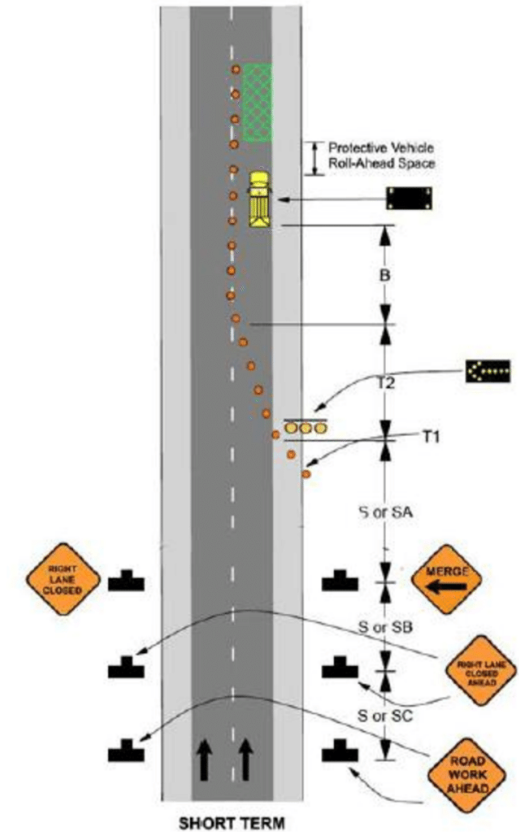

Key Project Elements & Timing

| Project Phases | Estimated Start – End Date |
|--|---------------------------------------|
| Permitting | Ongoing throughout Construction Phase |
| Construction | Late summer 2021 thru July 2022 |
| On-site treatment system assembly | June/July 2022 |
| Access Road Construction | Complete |
| Drill Extraction Wells | Complete |
| Site Work & Preparation for Treatment Building | Complete |
| Delivery & Construction of Treatment Building | Complete |
| Delivery & Installation of Filtration Technology | Complete |
| Extraction well pump placement - Temporary Lane Closures | June 2022 (delayed due to high water) |
| Final street repairs | Early May/June2022 |
| Complete Construction & Begin Startup of GETS | Goal: July 2022 |

Questions & Feedback



If you have any other questions, you can always call our dedicated phone line at [\(715\) 582-7100](tel:7155827100) or send an email via our website, [www.tycomarinette.com/Contact Us](http://www.tycomarinette.com/ContactUs)
