





**Fire Technology Center (FTC)  
PFAS Remediation Office Hours  
June 29, 2022**

**tyco**  
*Fire Protection Products*

# GETS Route – Well Locations & Piping Routes

-  = 9 extraction wells
-  = Conveyance pipes
-  = Ditch B
-  = Outfall



# GETS Construction Last Four Weeks

---

- Work continued at the GETS Treatment Building located on FTC property, including:
  - Final grading, drainage and seeding
  - Installed stainless steel pipe spool pieces and valves on GAC vessels
  - Ongoing installation of electrical lines and mechanical piping
  - Installation of large poly tanks
  - Sand filter installation
  - Clarifier installation
  - Concrete pad for dumpsters

# GETS Construction Last Four Weeks

---

- Control panels and electrical connections installed at extraction wells
- Completed paving restoration of Oak View Rd, GETS access road, and Marinette HS driveway
- Completed grading around extraction wells
- Landscaping at EX-6

# GETS Construction – Upcoming activities

---

- Finalizing electrical and piping in GETS building through end of July
- Extraction well pump installation end of June
- Extraction well EX-7 over drilling/repair in Edwin St – July 5<sup>th</sup> through 8<sup>th</sup>
- Equipment controls testing mid to late July
- System startup anticipated early to mid-August




# GETS Construction– Treatment Building





# GETS Construction– Treatment Building

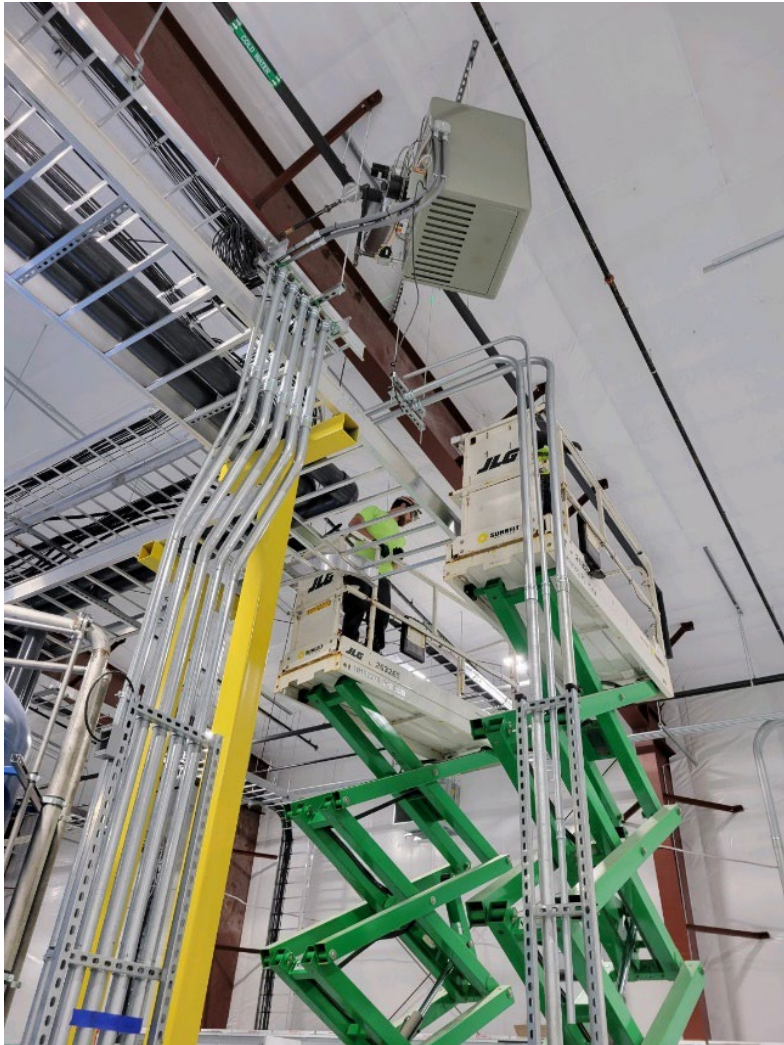




# GETS Construction– Treatment Building





# GETS Construction– Treatment Building

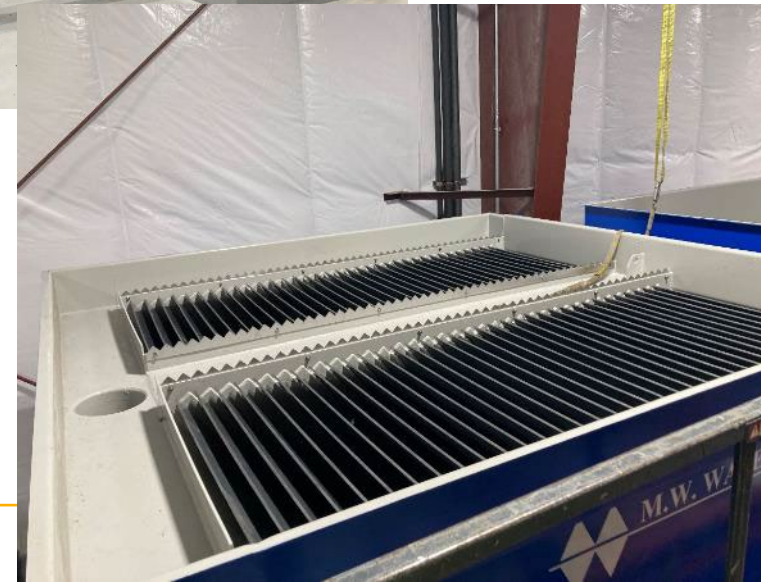



# GETS Construction– Treatment Building

---





# GETS Construction – Off Site





# GETS Construction – Off Site






# GETS Construction – Off Site





# Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security

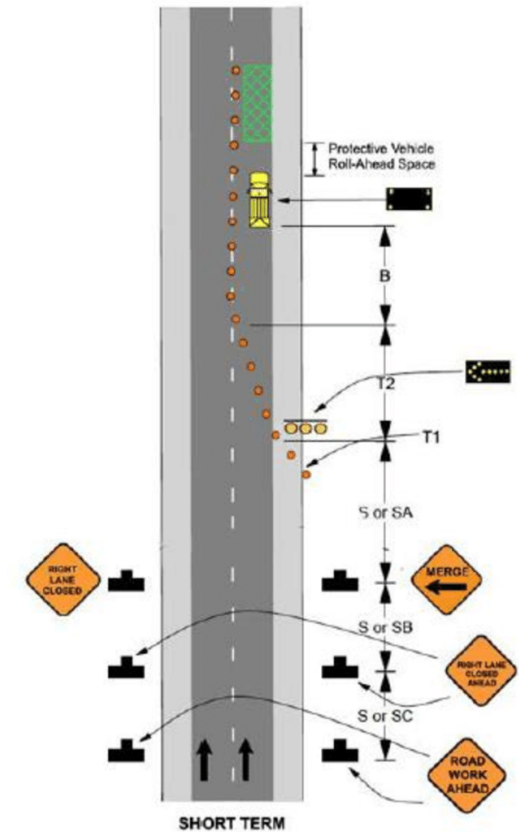



# Key Project Elements & Timing

Project Phases	Estimated Start – End Date
<b>Permitting</b>	Ongoing throughout Construction Phase
<b>Construction</b>	Late summer 2021 thru July 2022
On-site treatment system assembly	Through end of July 2022
Access Road Construction	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	Complete
Delivery & Installation of Filtration Technology	Complete
Extraction well pump placement - Temporary Lane Closures	Complete
Final street repairs	Complete
<b>Complete Construction &amp; Begin Startup of GETS</b>	Goal: July/August 2022



# Questions & Feedback

---



If you have any other questions, you can always call our dedicated phone line at [\(715\) 582-7100](tel:7155827100) or send an email via our website, [www.tycomarinette.com/Contact Us](http://www.tycomarinette.com/ContactUs)
