





**Fire Technology Center (FTC)
PFAS Remediation Office Hours
April 27, 2022**



GETS Route – Well Locations & Piping Routes

-  = 9 extraction wells
-  = Conveyance pipes (to be installed)
-  = Ditch B
-  = Outfall



GETS Construction Last Four Weeks

- Work continued in interior of Treatment Building located on FTC property, including:
 - All carbon & resin treatment vessels installed
 - Additional treatment equipment onsite and being installed
 - Filter press, air compressor
 - Clarifier later this week
 - Ongoing installation of electrical lines and mechanical piping
- Installation of all exterior groundwater conveyance piping complete
 - All exterior influent pipelines have been pressure tested and vaults moisture sealed
- Extraction well pumps delivered pending installation (due to high water levels)
- Electrical and mechanical piping completed within extraction well vaults


GETS Construction – Up coming activities

- Final restorations of roads will be completed late May / early June 2022
- Installation of extraction well pumps pending decrease in water levels
- Fiber optic and electric installed in conduit to wells weeks of May 9 & 16
 - Limited lane closures week of May 16th
- WPS electric and gas service upgrades on Edwin and Oak View ongoing
 - Unrelated to GETS project

GETS Construction– Treatment Building




GETS Construction – Piping/construction

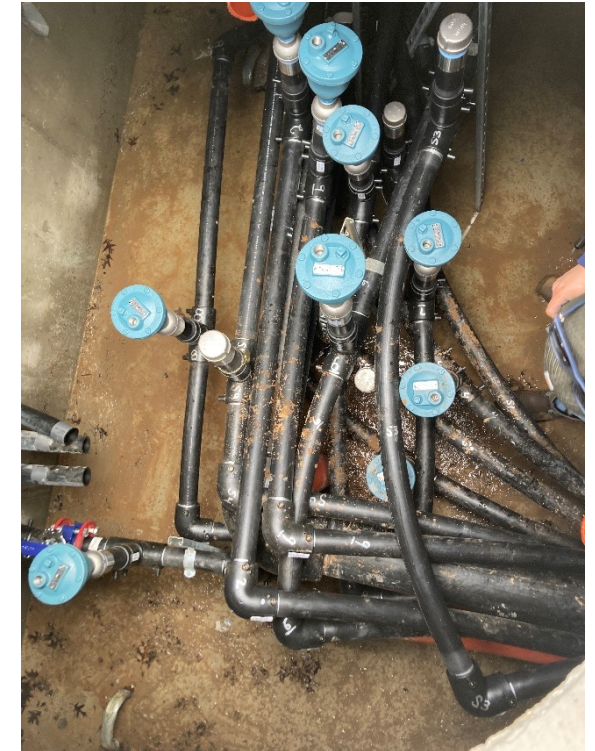

Safety First During Construction

- Community Outreach and Notifications
- Traffic Control
- Site Security

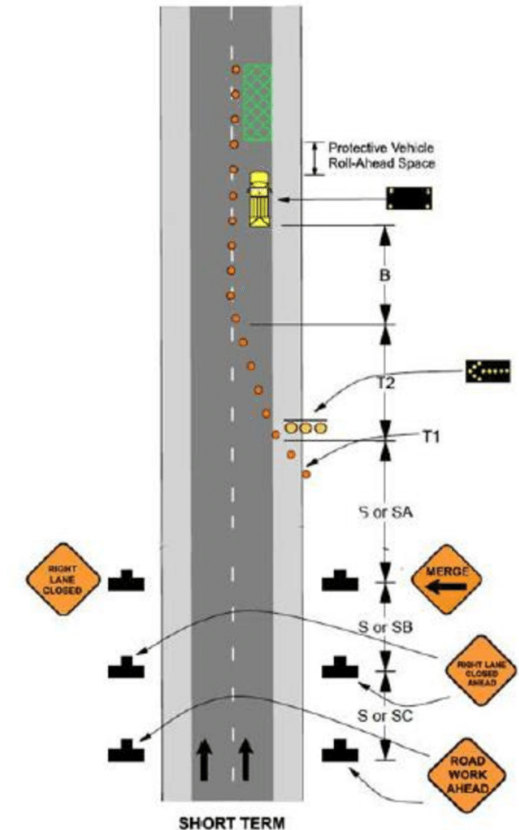

Key Project Elements & Timing

Project Phases

Estimated Start – End Date

Permitting	Ongoing throughout Construction Phase
Construction	Late summer 2021 thru July 2022
On-site treatment system assembly	June/July 2022
Access Road Construction	Complete
Drill Extraction Wells	Complete
Site Work & Preparation for Treatment Building	Complete
Delivery & Construction of Treatment Building	Complete
Delivery & Installation of Filtration Technology	Complete
Extraction well pump placement - Temporary Lane Closures	June 2022 (delayed due to high water)
Final street repairs	Early May/June 2022
Complete Construction & Begin Startup of GETS	Goal: July 2022

Questions & Feedback



If you have any other questions, you can always call our dedicated phone line at [\(715\) 582-7100](tel:7155827100) or send an email via our website, [www.tycomarinette.com/Contact Us](http://www.tycomarinette.com/ContactUs)
